



Green Certification Checklist



Park Models

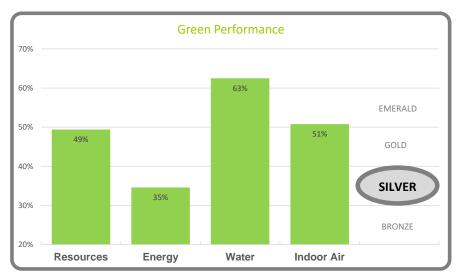



Resource Efficiency			
<u>Points</u> Available	<u>Item</u>	<u>Points</u> <u>Claimed</u>	
14	Construction materials are recycled offsite. (2 pts for each material, max 14 pts) list: wood, crdbrd, aluminum, steel, shingles, copper wire, vinyl siding	14	
20	Ratio of recycled materials to waste (50% - 5 pts, 75% - 10 pts, 90% - 20 pts)		
5	CNC Machines utilized to maximize material cuts list:		
5	Jigs are used (1 point each - max 5 points) list:		
5	Material scraps are reused. (max 5 points) list: carpet scraps, vinyl is resold, plywood/OSB/wood for backers	3	
5	Reusable shipping containers used for major materials (1 pt each, max 5) list: microwave boxes used to ship loose parts	1	
5	Major materials are cut to size at supplier - (1 pt each, max 5) list:		
10	Materials with recycled content are used. (2 pt each, max 10) list: vinyl siding, carpet	4	
10	Regional materials are used for major components (500 miles) - (2 pts each, max 10 pts) list: shingles, windows, cabinet doors, siding, OSB	10	
5	Component manufacturer facility is ISO 14001 or equivalent (1 pt each, max 5 pts)	2	
6	Certified wood (1 point per product type, max 6) list: OSB - CSA, plywood - FSC,lumber - SFI	6	
5	Tree planted for each registration		
	Resource Efficiency Total:	40	49%
Energy	Efficiency		
50	Insulation Type R-value	33	
	Walls batt 11 Floor batt 11		
30	Ceiling batt 11 Total: 33 LED lighting (>90%)		
20	Energy efficient appliances (5 points each, max 20)	10	
5	list: refrigerator, a/c Energy efficient furnace (95% AFUE or better or alternative heat)	10	
6	list: Skylights standard to provide natural lighting (2 pt each, max 6)		
10	Heating system with NO ducts		
10	Cooling system with NO ducts		
4	Convection microwave or cooktop is standard - (2 pts each, max 4)		
30	Solar panels (pre-wired - 10 pts; factory installed - 30 pts)		
5	Enhanced window performance		
3	Programmable Thermostat	3	
10	Rain Booth tested or soap tested for air tightness/leaks		
	Energy Efficiency Total:	46	35%

Water Efficiency

30 Low flow fixtures kitchen (≤ 2.2 gpm - 5 pts) bath (≤ 1.5 gpm - 5 pts) 5 showerhead (2.5 gpm - 5 pts) toilet is 1.6 gpf - 5 pts 5 toilet is composting - 10 points

20

5 Instant hot water heater is standard

Water line test water is recycled and reused or units are air tested

5

Water Efficiency Total:

25

63%


Indoor Air Quality

5

6

5

All wood materials are CARB 2 compliant - MANDATORY

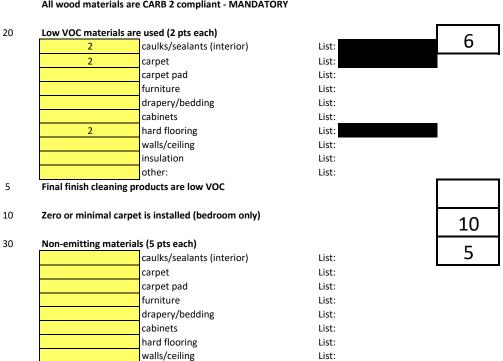

9 Mechanical ventilation/exhaust devices (3 pts each)

Kitchen exhaust vents to the outdoors

insulation

other:

3

List:

List:

Ductwork is off the floor (5 pts) or protected/vacuumed at final (3 pts)

6 3

Indoor Air Total:

33

51%
